RFI detail

#155 Office O236 - Roller Window Shade Confirmation

Status	**Closed**
Created on	Sep 12, 2025 by **Arianna Barile** (DPR Construction)
RFI type	Default RFI workflow
Ball in court	**Arianna Barile** (DPR Construction)
Answered	Sep 16, 2025 by **Arianna Barile** (DPR Construction)

Question

Per drawing P3-A04-10, a roller window shade is called out for on the South portion of the East wall in room 0236. Please confirm whether this location is correct.

Official response

Ashley Hill (Corgan - 10059759): Confirmed to remove the roller shade at 0236. GC to cost credit back to Owner. CS - CORGAN - 9.15.25

*By **Arianna Barile** (DPR Construction) - Sep 16, 2025, 9:37 AM PDT*

Official response attachments

RFI-155 - OFFICE O236 - ROLLER WINDOW SHADE CONFIRMATION - CORGAN.PDF, *Sep 16, 2025, 9:37 AM PDT*

References and Attachments

Files (1)

- RFI #155 - Office 0236 - Roller Window Shade Confirmation.pdf

Impact

Cost impact	No
Schedule impact	No

Other attributes

Priority	Normal
Discipline	Architectural
Category	-
Location	-
Location details	Office 0236
External ID	-
Co-reviewer(s)	-

Activities	By	At
Arianna Barile changed the status from **Open** Answered to **Closed** **Official response:** Ashley Hill (Corgan - 10059759): Confirmed to remove the roller shade at 0236. GC to cost credit back to Owner. CS - CORGAN - 9.15.25 changed the **official response attachment** to: RFI-155 - OFFICE O236 - ROLLER WINDOW SHADE CONFIRMATION - CORGAN.PDF .	**Arianna Barile**	Sep 16, 2025, 9:37 AM PDT
Arianna Barile changed the status from **Open** In Review to **Open** Answered set Ball in court to **Arianna Barile** (DPR Construction)	**Arianna Barile**	Sep 16, 2025, 9:37 AM PDT
Ashley Hill (Corgan - 10059759) response was submitted by **Arianna Barile**: Confirmed to remove the roller shade at 0236. GC to cost credit back to Owner. CS - CORGAN - 9.15.25 added the **response attachment** to: RFI-155 - OFFICE O236 - ROLLER WINDOW SHADE CONFIRMATION - CORGAN.PDF .	**Arianna Barile**	Sep 16, 2025, 9:37 AM PDT
Arianna Barile added a reference to a File **RFI #155 - Office 0236 - Roller Window Shade Confirmation.pdf**	**Arianna Barile**	Sep 12, 2025, 8:18 AM PDT
Arianna Barile (DPR Construction) created this RFI in **Open** In Review status and set Ball in court to **Ashley Hill** (Corgan - 10059759).	**Arianna Barile**	Sep 12, 2025, 8:18 AM PDT

RFI Transmittal

23559.0000, CoreSite SV9 - Phase 3

Date Sent	9/16/2025
Subject	Office O236 - Roller Window Shade Confirmation
RFI Id	RFI-155
Type	RFI
Transmittal Id	00518
Purpose	Answered
Via	Info Exchange

Question

Suggestion

Answer

Please follow the provided link to download the design team response to RFI-155 - Office O236 - Roller Window Shade Confirmation. Please let us know if you have any additional questions or comments.

Thank you,

ASHLEY HILL
Construction Administration Specialist
Corgan

FROM

Name	Company	Email	Phone
Ashley Hill	Corgan	Ashley.Hill@corgan.com	214-977-3589

TO

Name	Company	Email	Phone
Leo Dickson	DPR Construction, Inc.	leod@dpr.com	
Arianna Barile	DPR Construction, Inc.	ariannab@dpr.com	
David Vu	DPR Construction, Inc.	davidvu@dpr.com	
Mariana Simmonds	DPR Construction, Inc.	marianas@dpr.com	

DESCRIPTION OF CONTENT

QTY	Dated	Title	Number	Scale	Size
1	9/15/2025	RFI-155 - Office O236 - Roller Window Shade Confirmation - CORGAN.pdf			

COPIES

Ashley Hill (Corgan)
Celine Shoudel (Corgan)
Justin Cain (Corgan)
Mike Hemme (Corgan)
Sevrin Scarcelli (Corgan)
Will Roarty (Corgan)

RFI detail

#155 Office O236 - Roller Window Shade Confirmation

Status	**Open** In Review
Created on	Sep 12, 2025 by **Arianna Barile** (DPR Construction)
RFI type	Default RFI workflow
Ball in court	**Ashley Hill** (Corgan - 10059759)
Due date	Sep 18, 2025

Question

Per drawing P3-A04-10, a roller window shade is called out for on the South portion of the East wall in room 0236. Please confirm whether this location is correct.

References and Attachments

Files (1)

- RFI #155 - Office 0236 - Roller Window Shade Confirmation.pdf

Impact

Cost impact	No
Schedule impact	No

Other attributes

Priority	Normal
Discipline	Architectural
Category	-
Location	-
Location details	Office 0236

External ID	-
Co-reviewer(s)	-

Activities	By	At
Arianna Barile added a reference to a File **RFI #155 - Office 0236 - Roller Window Shade Confirmation.pdf**	**Arianna Barile**	Sep 12, 2025, 8:18 AM PDT
Arianna Barile (DPR Construction) created this RFI in **Open** In Review status and set Ball in court to **Ashley Hill** (Corgan - 10059759).	**Arianna Barile**	Sep 12, 2025, 8:18 AM PDT

Confirmed to remove the roller shade at 0236. GC to cost credit back to Owner.

CS - CORGAN - 9.15.25

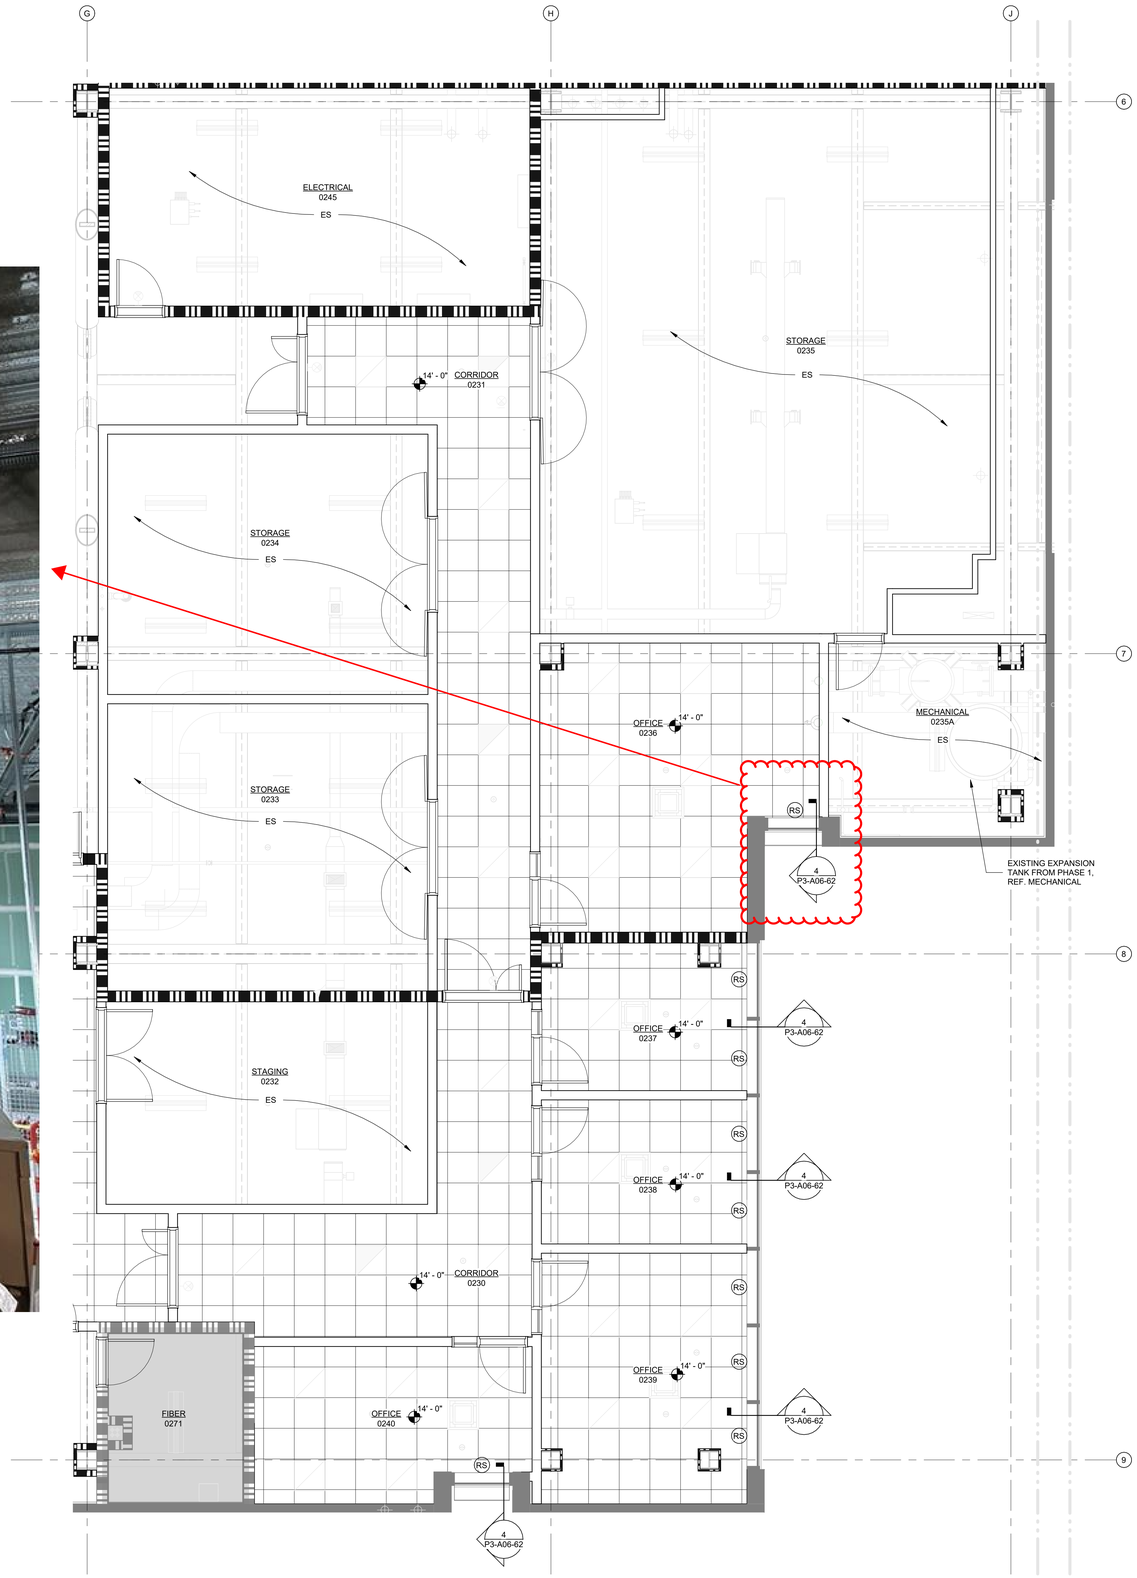

1 ENLARGED REFLECTED CEILING PLAN - TENANT OFFICES
1/4" = 1'-0"

RCP LEGEND

2X2 LAY-IN CEILING	GYP. BD. CEILING
ES EXPOSED STRUCTURE	CLG MOUNTED CURTAIN TRACK
2X2 LAY-IN INDIRECT FIXTURE	2X4 LAY-IN INDIRECT FIXTURE
1X4 LAY-IN INDIRECT FIXTURE	RECESSED LIGHT FIXTURE
2X2 LAY-IN PARABOLIC FIXTURE	2X4 LAY-IN PARABOLIC FIXTURE
1X4 HUNG PARABOLIC STRIP	RECESSED WALLWASHER
2X2 LAY-IN LENS FIXTURE	2X4 LAY-IN LENS FIXTURE
1X4 LAY-IN LENS FIXTURE	HANGING PENDANT LIGHTING FIXTURE
WALL SCONCE TOP @ 7' - 2" A.F.F.	COVE LIGHTING
1' - 0" FINISHED CEILING HEIGHT A.F.F.	SUPPLY AIR DIFFUSER
RETURN AIR DIFFUSER	EMERGENCY EXIT FIXTURE
CEILING SPEAKER	RS AUTOMATIC ROLLER SHADE

GENERAL RCP NOTES

1 CEILING HEIGHTS ARE 9'-0" A.F.F. UNLESS NOTED OTHERWISE.
2 THE ROOM FINISH SCHEDULE TYPICALLY INDICATES CEILING MATERIALS AND FINISHES. MATERIALS OR FINISHES THAT VARY WITHIN A ROOM WILL BE INDICATED ON THE R.C.P.
3 R.C.P.'S WILL TYPICALLY INDICATE:
A. LOCATIONS, DIMENSIONS AND HEIGHTS A.F.F. OR FURREDOWNS.
B. VARYING CEILING MATERIALS AND THEIR LOCATIONS.
C. HEIGHTS OF WALLS A.F.F. (FULL HEIGHT AND PARTIAL HEIGHT).
D. REQUIRED FIRE-RATINGS OF WALLS.
E. FINAL LOCATIONS OF CEILING MOUNTED FIXTURES/ DEVICES.
4 WHERE WALL TYPE FIRE-RATING DESIGNATIONS FROM THE FLOOR PLANS CONFLICT WITH THE FIRE-RATING DESIGNATIONS INDICATED ON THE R.C.P., THE MORE STRINGENT DESIGNATIONS SHALL APPLY.
5 PROVIDE ADDITIONAL SUPPORT FOR TRACK LIGHTING AS REQUIRED.
6 COORDINATE MEP / ETC. DRAWINGS FOR ALL FIXTURES/ DEVICES MOUNTED IN, ABOVE, OR HUNG FROM THE CEILING. FINAL FIXTURE/DEVICE LOCATIONS ARE DETERMINED BY THE ARCHITECTURAL R.C.P. WHERE CONDITIONS DIFFER SIGNIFICANTLY BETWEEN THE PLANS, REQUEST CLARIFICATION FROM THE ARCHITECT BEFORE PROCEEDING. WHERE FIXTURES/ DEVICES SHOWN OR SPECIFIED ON DRAWINGS OTHER THAN THE ARCHITECTURAL R.C.P.'S ARE VISIBLE AT THE CEILING PLANE, COORDINATE LOCATIONS WITH THE ARCHITECT.
7 DO NOT INSTALL CEILING GRID UNTIL WORK ABOVE CEILING IS COORDINATED AND INSTALLED WITHIN AVAILABLE PLENUM SPACE.
8 LOCATE CEILING MOUNTED FIXTURES/ DEVICES IN THE CENTERS OF FULL CEILING PANELS U.N.O.
9 LIGHT FIXTURES IN MECHANICAL AND EQUIPMENT ROOMS ARE SHOWN FOR QUANTITY ONLY. CONTRACTOR IS TO COORDINATE FIXTURE PLACEMENT WITH ALL MEP ITEMS AND SET FINAL FIXTURE LOCATIONS AS REQUIRED TO EVENLY AND FULLY LIGHT ACCESSIBLE AREAS OF THE ROOM WITH THE QUANTITY OF FIXTURES SHOWN.
10 PROJECTION SCREENS TO BE CEILING MOUNTED, CENTERED ABOVE MARKER BOARD, U.N.O.
11 GYP. CEILINGS AND BULKHEADS TO BE PAINTED PER FINISH PLANS, U.N.O.
12 ACCENT PAINT ON GYP. BOARD BULKHEADS TO BE ON BOTTOM AND SIDES OF BULKHEAD.
13 ALL INTERIOR PARTITIONS ARE TO BE TO DECK, U.N.O.
14 REFER TO MECHANICAL PLANS FOR TRANSFER AIR OPENING SIZE (FREE AREA) AND LOCATIONS WHERE REQUIRED

SCOPE EXTENTS LEGEND

PREVIOUS BUILD AREAS NOT UNDER PROJECT SCOPE. PERMITTED UNDER SEPARATE PERMIT

NEW CONSTRUCTION SV9 - PHASE PROJECT SCOPE

PARTITION LEGEND

NEW PARTITION
EXISTING PARTITION
DEMOLISHED PARTITION
TEMPORARY PARTITION
PARTIAL HEIGHT PARTITION

WALL RATING LEGEND

UNRATED WALL ASSEMBLY
1 HR RATED FIRE BARRIER ASSEMBLY
2 HR RATED FIRE BARRIER ASSEMBLY
3 HR RATED FIRE BARRIER ASSEMBLY
1 HR RATED SMOKE BARRIER ASSEMBLY

FINISH LEGEND

CPT-1
CT-1
RAF-1
L CORNER GUARD
SC-1
E FLOOR TRANSITION, SEE TRANSITION SCHEDULE

CORGAN

kW mission critical engineering

PEOPLES ASSOCIATES
STRUCTURAL ENGINEERS

Kimley»Horn
Expect More. Experience Better.

	ISSUES	
1	10.10.2024	90% DESIGN DEVELOPMENT
2	10.31.2024	ISSUE FOR PERMIT
3		
4		
5		
6		
7		
8		
9		
10		

	REVISIONS	

NOT FOR CONSTRUCTION

Date of issue:
10.31.2024

CORESITE SV9
PHASE 3
CORESITE
2915 STENDER WAY, SANTA CLARA, CA

KEYPLAN



ENLARGED REFLECTED CEILING PLANS

JOB 23559.0000
DATE 10.10.2024
SHEET

P3-A04-10

10/31/2024 4:57:08 PM P3-A04-10 ENLARGED REFLECTED CEILING PLANS
